


## MEASURE B BOND PROGRAM SUMMARY UPDATE

WEDNESDAY, FEBRUARY 5, 2019

Project	Scope	Schedule	Status
<b>PROJECTS UNDER CONSTRUCTION WINTER 2019:</b>			
<b>Athletic Turf Fields (Phase II)</b>	Baseball Field	Completion: March 2019	<ul style="list-style-type: none"> <li>• <i>Site Work: paving, bleacher installation, turf installation</i></li> </ul>
<b>Pomo Cluster Phase II</b>	Interior Renovations	Completion: Summer 2019	<ul style="list-style-type: none"> <li>• <i>Interior framing complete, MEP systems installation ongoing, furniture selections</i></li> </ul>
<b>Miwok Center</b>	New Construction	Completion: Summer 2020	<ul style="list-style-type: none"> <li>• <i>Removal of site utilities, installation of water line, ongoing grading activities</i></li> </ul>
<b>Admin Center Roof Replacement</b>	Roof Replacement	Completion: March 2019	<ul style="list-style-type: none"> <li>• <i>Sloped roofing demolition complete, roofing construction in progress</i></li> </ul>
<b>Building 27 Painting</b>	Exterior Painting	Completion: Spring 2019	<ul style="list-style-type: none"> <li>• <i>Contract awarded, pending NTP, scheduling project to begin</i></li> </ul>
<b>PROJECTS BIDDING SPRING &amp; SUMMER OF 2019:</b>			
<b>Site Improvements</b>	Widening Fire Lane at PE Complex	Rebidding	<ul style="list-style-type: none"> <li>• <i>Prior bid was high, preparing project for rebidding</i></li> </ul>
<b>Admin Cluster 9 &amp; 12 Design</b>	Tenant Improvements	Request for Proposal from A&E Firms	<ul style="list-style-type: none"> <li>• <i>Scope will involve abatement, MEP upgrades, tenant improvements</i></li> </ul>
<b>Maintenance &amp; Operations</b>	New Construction	Bidding: Spring 2019	<ul style="list-style-type: none"> <li>• <i>DSA Approval pending within a week</i></li> </ul>
<b>PROJECTS IN DESIGN WINTER 2019:</b>			
<b>Performing Arts</b>	AV System Upgrades	Construction: Summer 2019	<ul style="list-style-type: none"> <li>• <i>Project currently in the Design Phase</i></li> </ul>
<b>Jonas Center &amp; Building 18</b>	Repurposing and New Construction	Construction: Spring 2019	<ul style="list-style-type: none"> <li>• <i>DSA Review Pending and finalizing Rotary Design Changes</i></li> </ul>
<b>Fusselman Hall</b>	Structural and Waterproofing Improvements	Design-Bid-Build Construction: Fall 2019	<ul style="list-style-type: none"> <li>• <i>Project currently in the Design Phase</i></li> </ul>
<b>Learning Resource Center</b>	New Construction / Replacement Building for LRC	<u>Prequals Due:</u> February 19, 2019 <u>Proposals Due:</u> April 5, 2019	<ul style="list-style-type: none"> <li>• <i>RFP/Q currently advertised, addressing questions via Addendums posted on PlanetBids</i></li> </ul>

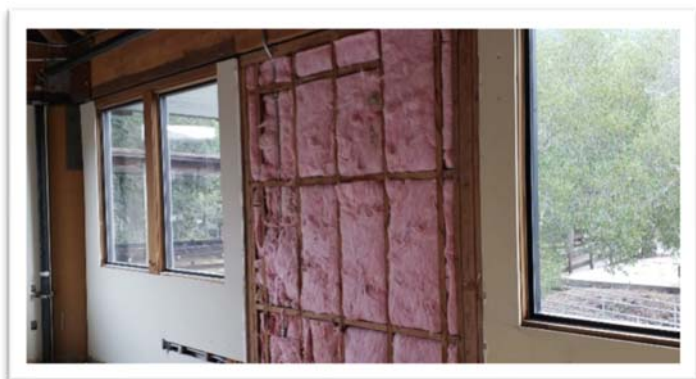

**Pomo Cluster Phase II - Construction**

**Athletic Turf Fields - (Phase II) Construction**



**Miwok Center - Site Improvements**

**Admin Cluster – Roofing Replacement**
